Full material list

Room: ≈ 94 1/2 in × ≈ 122 1/16 in · **Stock tile:** ≈ 23 5/8 in × ≈ 23 5/8 in
Grout: ≈ 1/16 in · Saw kerf: 0 in · Layout origin: Top left · Rotation: locked
24 installed pieces · 8 tiles per box · Reserve (%): 10% · Box price (USD): $12.50

Estimate	Opened	Reserve	Target	Boxes	Supplied	Box surplus	Total (USD)
Conservative	24	3	27	4	32	5	$50.00
Verified plan	21	3	24	3	24	0	$37.50

Before ordering, confirm actual tile size, tiles per box, dye lot and box price with the supplier. Spare tiles are whole stock held back, not saw waste. Box surplus is additional to that reserve.

Installation layout

Room plan · ≈ 94 1/2 in × ≈ 122 1/16 in

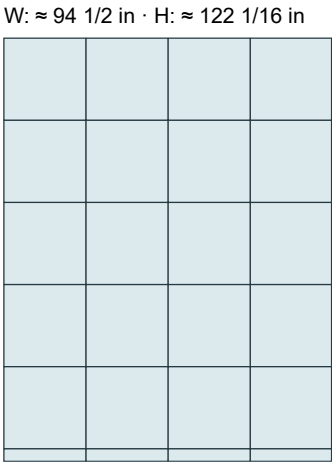

Room coordinates start at the top left; x increases right and y increases down.

Installed material

Piece	X	Y	Cut size
r0c0	0 in	0 in	≈ 23 5/8 in × ≈ 23 5/8 in
r0c1	≈ 23 11/16 in	0 in	≈ 23 5/8 in × ≈ 23 5/8 in
r0c2	≈ 47 3/8 in	0 in	≈ 23 5/8 in × ≈ 23 5/8 in
r0c3	≈ 71 1/8 in	0 in	≈ 23 3/8 in × ≈ 23 5/8 in
r1c0	0 in	≈ 23 11/16 in	≈ 23 5/8 in × ≈ 23 5/8 in
r1c1	≈ 23 11/16 in	≈ 23 11/16 in	≈ 23 5/8 in × ≈ 23 5/8 in
r1c2	≈ 47 3/8 in	≈ 23 11/16 in	≈ 23 5/8 in × ≈ 23 5/8 in

Piece	X	Y	Cut size
r1c3	≈ 71 1/8 in	≈ 23 11/16 in	≈ 23 3/8 in × ≈ 23 5/8 in
r2c0	0 in	≈ 47 3/8 in	≈ 23 5/8 in × ≈ 23 5/8 in
r2c1	≈ 23 11/16 in	≈ 47 3/8 in	≈ 23 5/8 in × ≈ 23 5/8 in
r2c2	≈ 47 3/8 in	≈ 47 3/8 in	≈ 23 5/8 in × ≈ 23 5/8 in
r2c3	≈ 71 1/8 in	≈ 47 3/8 in	≈ 23 3/8 in × ≈ 23 5/8 in
r3c0	0 in	≈ 71 1/8 in	≈ 23 5/8 in × ≈ 23 5/8 in
r3c1	≈ 23 11/16 in	≈ 71 1/8 in	≈ 23 5/8 in × ≈ 23 5/8 in
r3c2	≈ 47 3/8 in	≈ 71 1/8 in	≈ 23 5/8 in × ≈ 23 5/8 in
r3c3	≈ 71 1/8 in	≈ 71 1/8 in	≈ 23 3/8 in × ≈ 23 5/8 in
r4c0	0 in	≈ 94 13/16 in	≈ 23 5/8 in × ≈ 23 5/8 in
r4c1	≈ 23 11/16 in	≈ 94 13/16 in	≈ 23 5/8 in × ≈ 23 5/8 in
r4c2	≈ 47 3/8 in	≈ 94 13/16 in	≈ 23 5/8 in × ≈ 23 5/8 in
r4c3	≈ 71 1/8 in	≈ 94 13/16 in	≈ 23 3/8 in × ≈ 23 5/8 in
r5c0	0 in	≈ 118 1/2 in	≈ 23 5/8 in × ≈ 3 9/16 in
r5c1	≈ 23 11/16 in	≈ 118 1/2 in	≈ 23 5/8 in × ≈ 3 9/16 in
r5c2	≈ 47 3/8 in	≈ 118 1/2 in	≈ 23 5/8 in × ≈ 3 9/16 in
r5c3	≈ 71 1/8 in	≈ 118 1/2 in	≈ 23 3/8 in × ≈ 3 9/16 in
